
ROADPRO v3.6

Test Report

The error report, fixed and re-tested — plus every step of the user guide

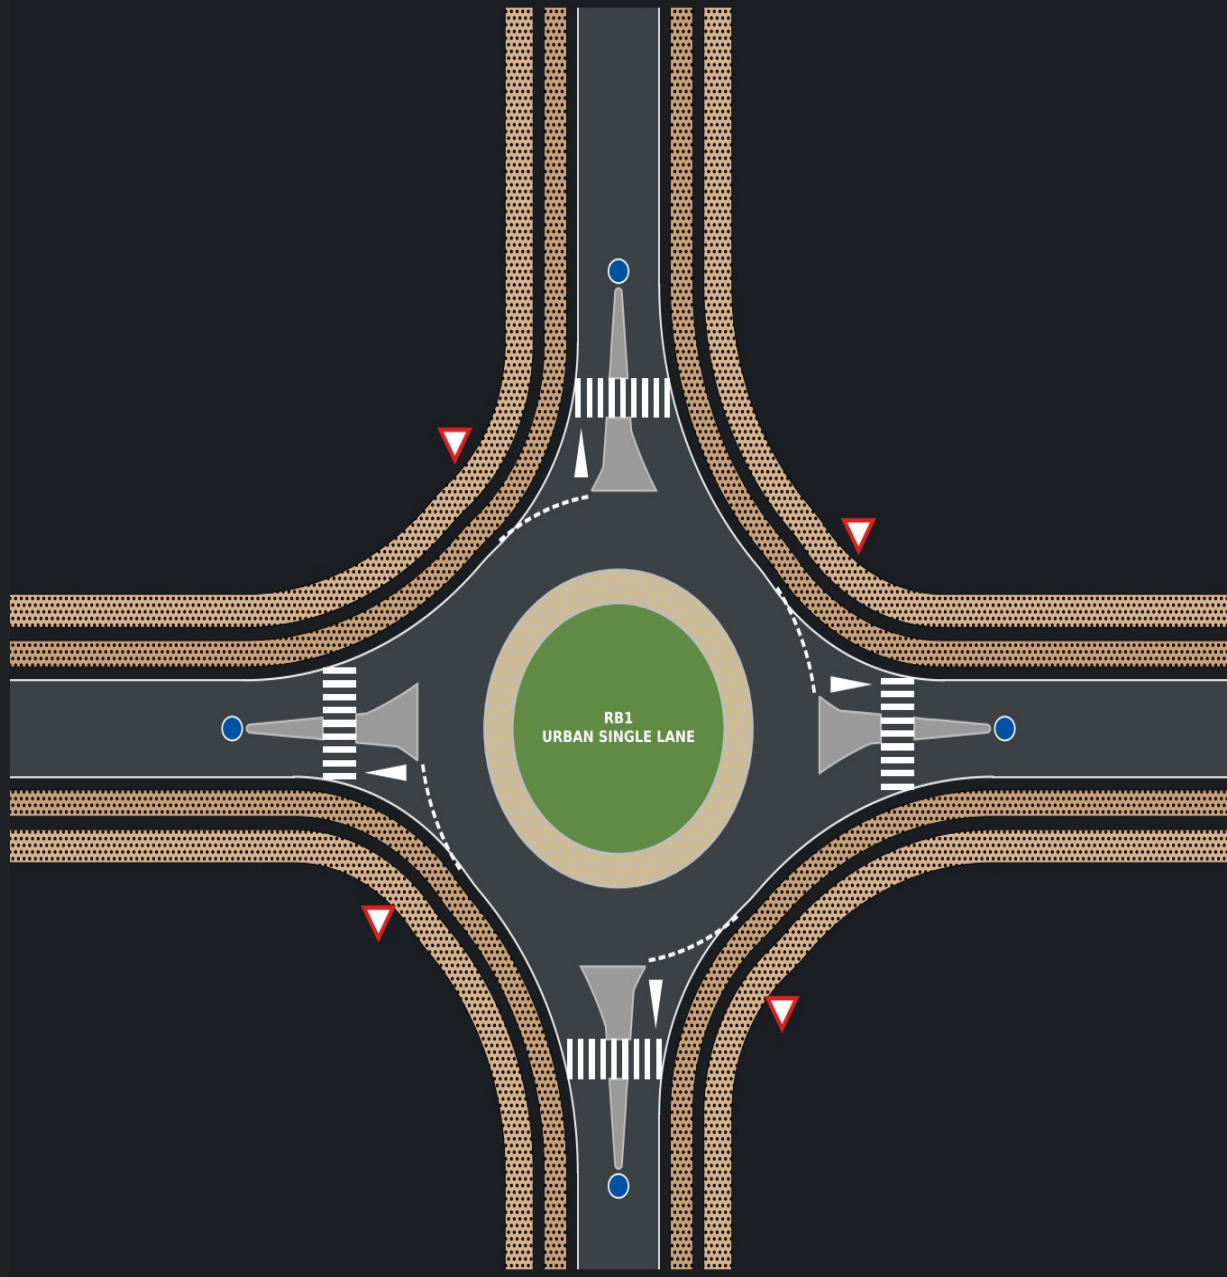

Test date 11-Nov-2026 · RoadPro.lsp v3.6 (9,149 lines)

Developed by https://www.exceltokml.com/

Result at a glance

156	155	0	9
checks run	passed	failed	report items fixed

Verdict: ready for the field test in AutoCAD / Civil 3D

All 155 automated checks pass: the full v3.5 regression plus 34 new drawing checks on the cases of the error report (15 of them fail on v3.5 — the faults you reported — and pass on v3.6). Updated RoadPro.lsp is in both packages.

01	02	03	04	05	06	07	08	09	10
22/22	18/18	21/21	5/5	16/16	22/22	5/5	3/3	9/9	34/34
Install	Build a road	Corridor & pavement	Widening & tapers	Junctions	Roundabouts	Live update	Lines & labels	Code & docs	Error report

How every step was tested

METHOD

Ran the real plugin code

RoadPro.lsp was loaded in an AutoLISP interpreter on a headless AutoCAD drawing engine. The real commands (RDP, RDJ, RDRB, RDER, RDX, live update) drew every case of the error report.

Opened every dialog

Each dialog was built from the DCL the plugin writes. Every tile key was checked, every button and list action fired, OK pressed — and invalid input typed to see it refused.

Checked the numbers

The drawings were measured: hatch overlaps (m²), barricades inside a carriageway or overlapping, curve tangency at every arc end, section extent and dimensions — plus the AASHTO / FHWA values.

Checked package & code

Add-in bundle, PackageContents.xml, installer scripts, shortcuts sheet and user guide were inspected; the whole file was scanned for syntax, undefined calls, argument counts and case clashes.


LIMIT AutoCAD itself cannot run here: the drawing engine is a faithful simulation (geometry, hatches, xdata, reactors), so a short field test in AutoCAD is still listed at the end. The same 34 drawing checks were also run on v3.5 to prove they catch the reported faults.


Error report — every item and its fix

Item	Reported	What v3.6 does	Test	Status
Pic 1	Junction walkway & hatch mismatch, should match	Side road starts at the kerb returns; strips and corner pieces meet	10.1	FIXED
Pic 2	Hatch should be merged with the tie-in road hatch	One mouth hatch joined to the main road hatch, no overlap	10.1	FIXED
Pic 3	Walk hatch mismatch; red & white line should auto adjust	Main road surface, shoulders, barricades and edge lines cut at the ring	10.2	FIXED
Pic 4	Roundabout finishing, hatch, pro look, full marking	Edge lines, inner ring line, entry arrows, give way; clean hatches	10.2	FIXED
Pic 5	Edit curve radius — barricades do not adjust	Bend refitted tangent after grip edit / RDER; barricades follow	10.4	FIXED
List	Keep always clean at tie-in, hatch not overlap	Pairwise hatch overlap 0.00 m² in every junction / roundabout test	10.1–10.2	FIXED
List	Add three and four way roundabout	2-way, T left, T right, cross; Automatic legs at 90°	10.2–10.3	FIXED
List	Section only up to corridor limit with pro dimension	Corridor limit, named chain, roadside / carriageway / corridor, level table	10.5	FIXED
List	Move centre line — all related things update	Junction head and roundabout legs follow the moved road	10.1	FIXED

Before / after — Junction tie-in, 60° skew, R 30

v3.5 → v3.6

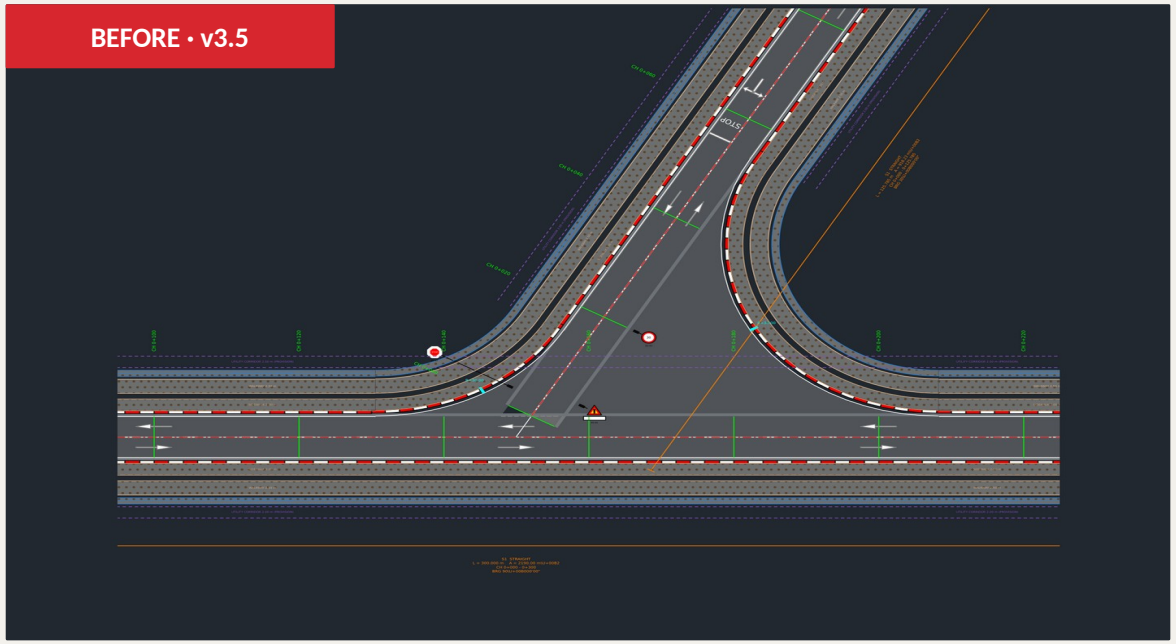


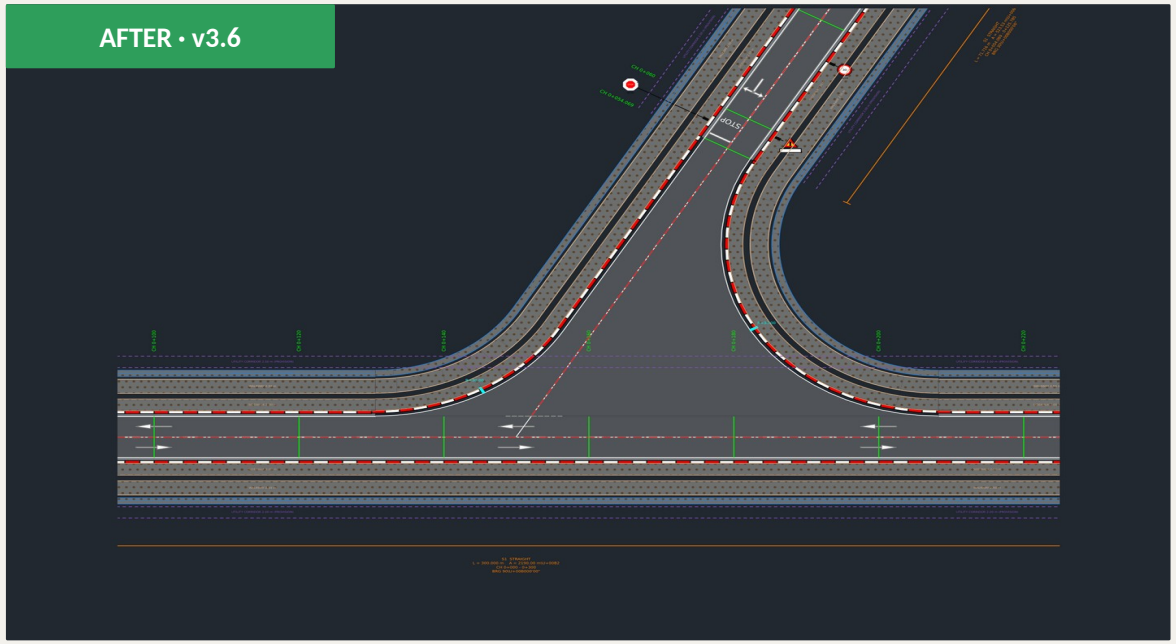


Measured check	v3.5	v3.6
Road surface hatches do not overlap (one clean mouth)	× 4 surface hatches, overlap 3.85 m2	✓ 3 surface hatches, overlap 0.00 m2
No barricade inside the carriageways	✓ 400 barricade units, 0 inside a travelled way	✓ 401 barricade units, 0 inside a travelled way
Barricade units do not overlap	✓ 0 overlapping pairs	✓ 0 overlapping pairs
Sidewalk strips meet the corner pieces	✓ sidewalk: 32 hatches in 3 connected group(s), overlap 0.00 m2	✓ sidewalk: 45 hatches in 3 connected group(s), overlap 0.00 m2
Walkway strips meet the corner pieces	✓ walkway: 32 hatches in 3 connected group(s), overlap 0.00 m2	✓ walkway: 45 hatches in 3 connected group(s), overlap 0.00 m2

Before / after — Roundabout on a road, 3-way (T)

v3.5 → v3.6

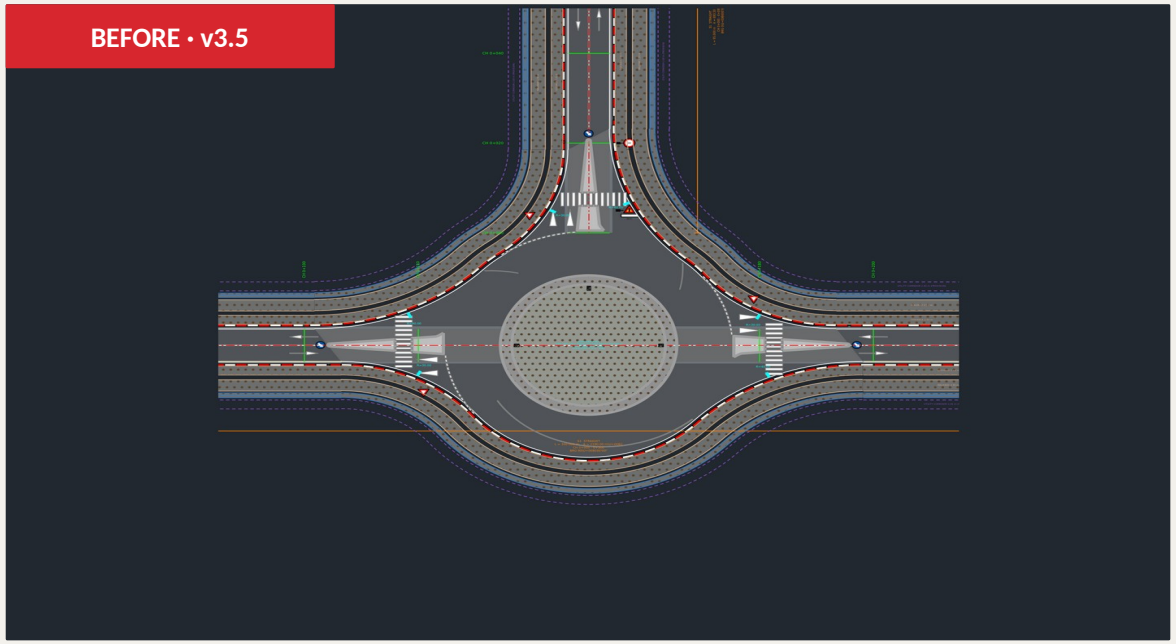

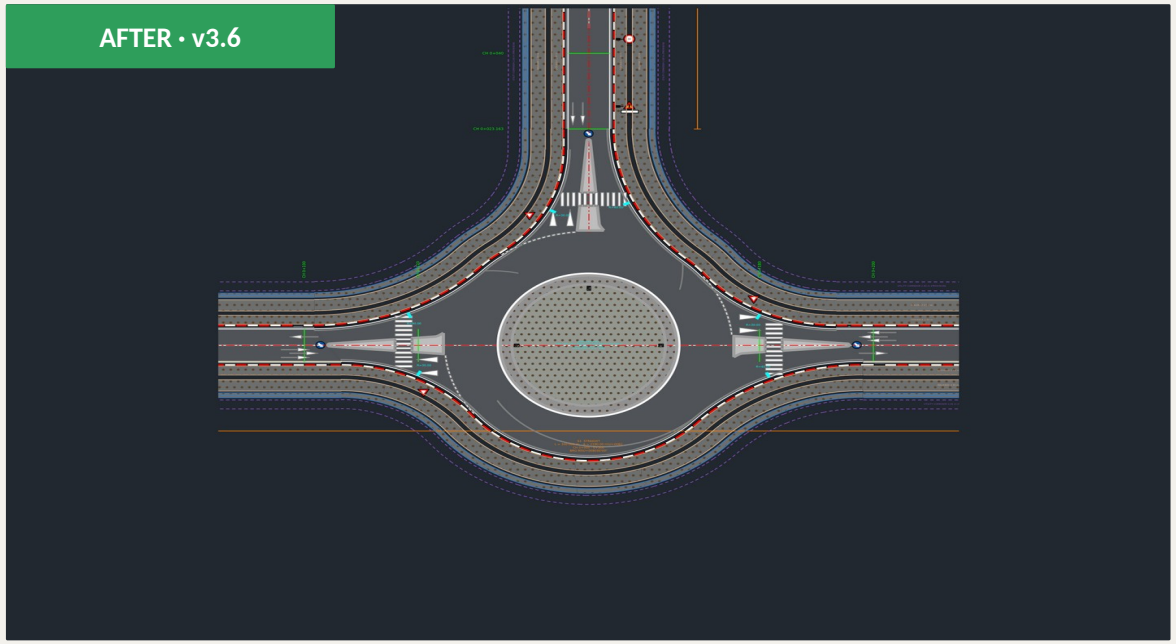


Measured check	v3.5	v3.6
Main road surface is cut at the ring (no double hatch)	× 3 surface hatches, overlap 597.10 m2	✓ 4 surface hatches, overlap 0.00 m2
No barricade runs into the roundabout	✓ 401 barricade units, 0 inside the ring	✓ 398 barricade units, 0 inside the ring
Barricade units do not overlap	× 3 overlapping pairs	✓ 0 overlapping pairs
Sidewalk hatches do not overlap	✓ 30 hatches, overlap 0.00 m2	✓ 55 hatches, overlap 0.00 m2
Full marking drawn	✓ 290 marking objects (edge lines, ring line, arrows, give way)	✓ 303 marking objects (edge lines, ring line, arrows, give way)


Before / after — Roundabout, automatic 4-way legs

v3.5 → v3.6

BEFORE · v3.5

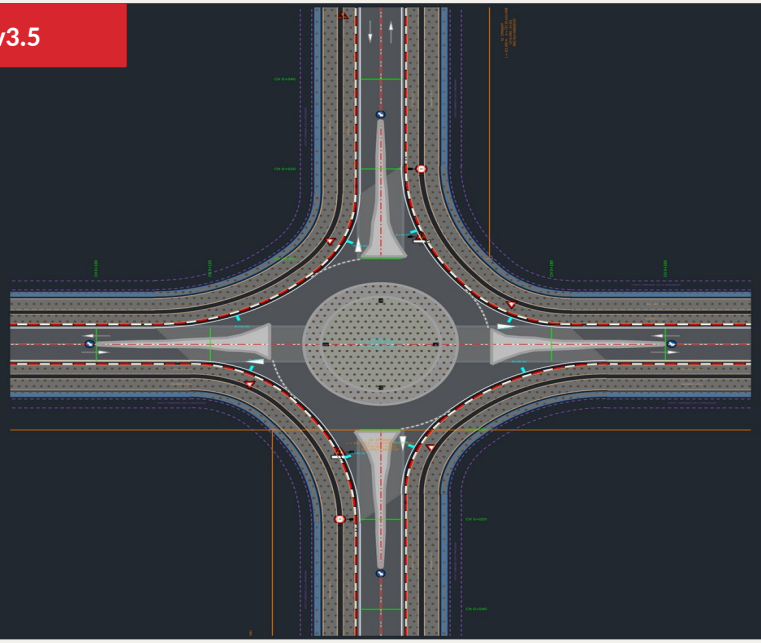

AFTER · v3.6

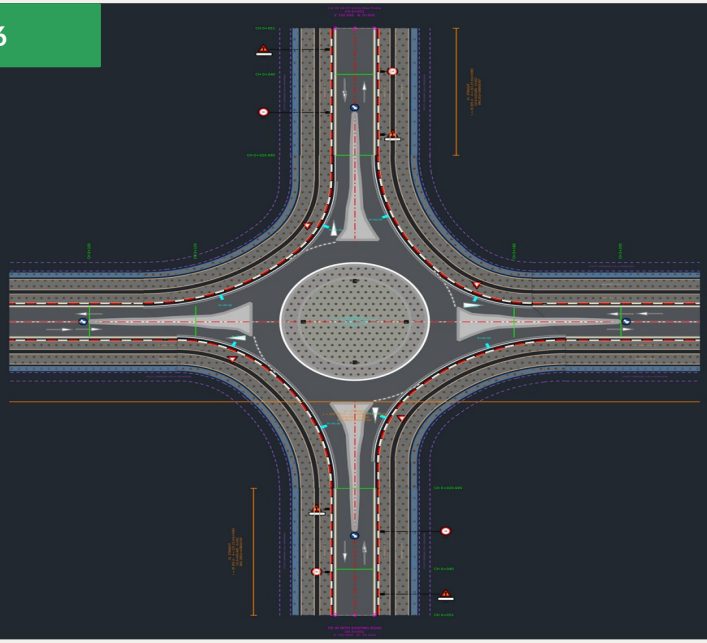


Measured check	v3.5	v3.6
Two side roads made at 90 degrees, 70 m	× 0 side roads ending at (150, +/-70); error no scripted input for entse	✓ 2 side roads ending at (150, +/-70)
No barricade inside the ring or overlapping	× 300 units, 0 overlapping	✓ 396 units, 0 overlapping


Before / after — Grip edit of a curve + live update

v3.5 → v3.6

BEFORE · v3.5

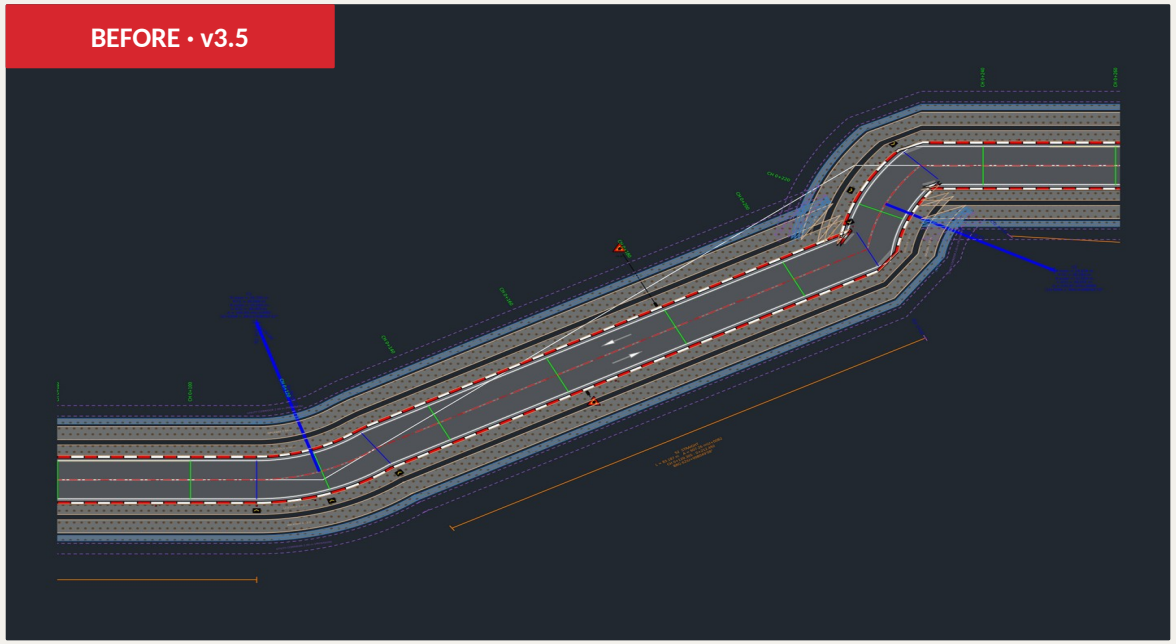


AFTER · v3.6

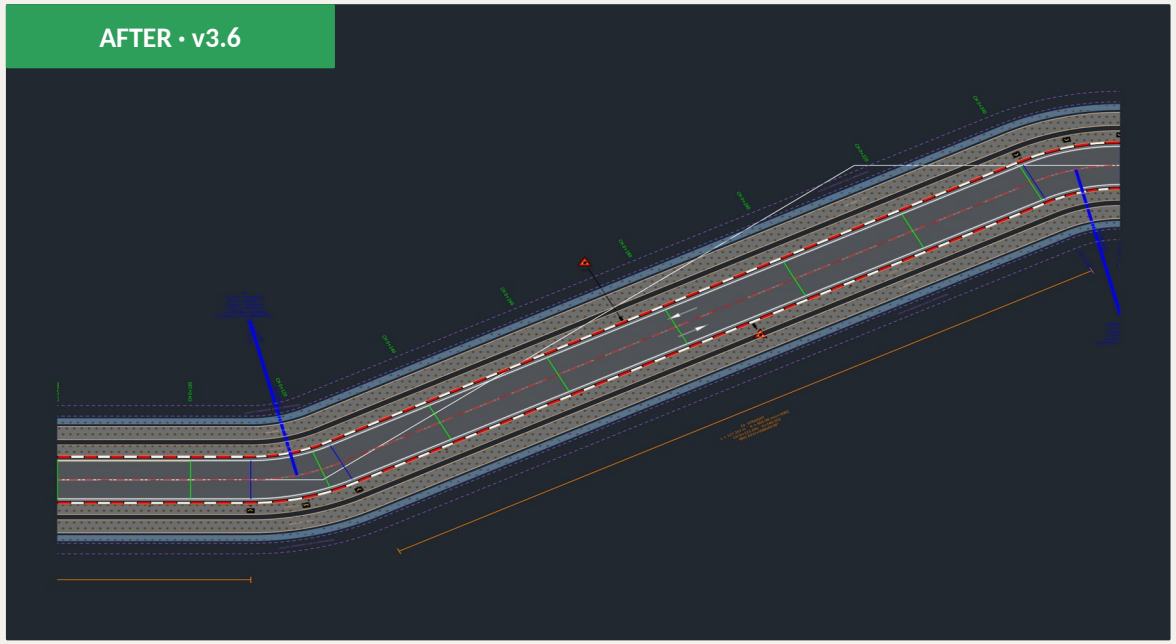

Measured check	v3.5	v3.6
Grip vertex: curve stays tangent	× largest kink at a curve end 54.69 deg	✓ largest kink at a curve end 0.00 deg
Grip vertex: barricades follow without crossing	× 322 units, 5 overlapping pairs	✓ 314 units, 0 overlapping pairs
Grip bulge: curve stays tangent	× largest kink at a curve end 7.31 deg	✓ largest kink at a curve end 0.00 deg
Grip bulge: barricades follow without crossing	✓ 318 units, 0 overlapping pairs	✓ 318 units, 0 overlapping pairs
RDER radius 60	✓ barricades follow : radii now [30.0, 60.0], 0 overlapping barricade pa	✓ barricades follow : radii now [30.0, 60.0], 0 overlapping barricade pa

Before / after — Cross section (RDX)

BEFORE · v3.5

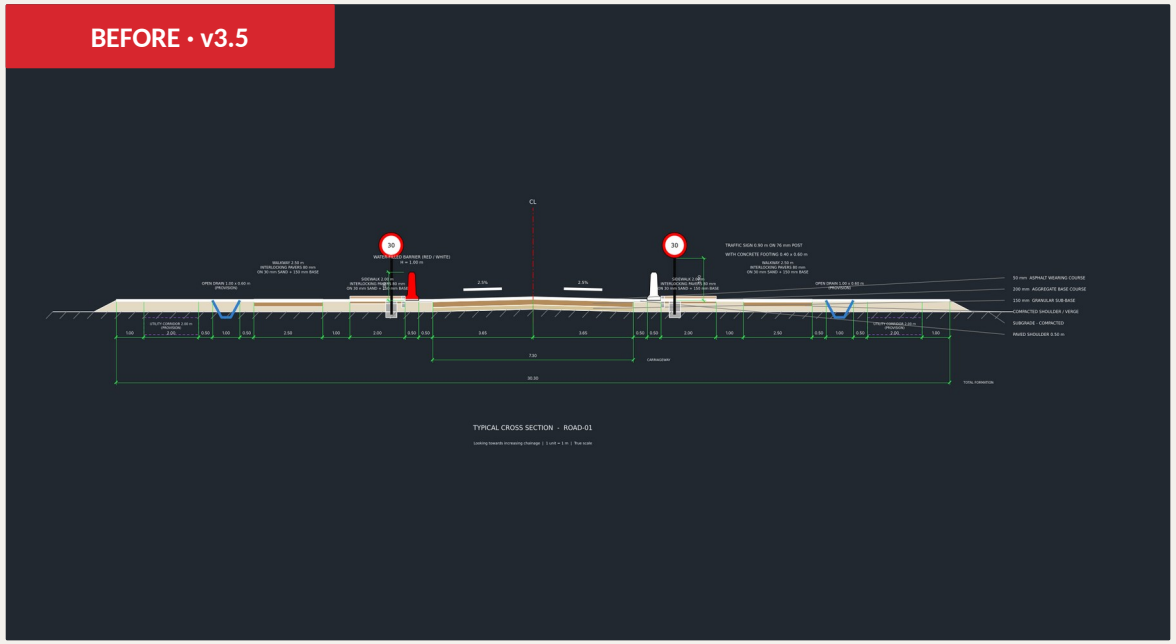

AFTER · v3.6



Measured check	v3.5	v3.6
Section geometry stops at the corridor limit (14.15 m)	× outermost section point 17.450 m from CL	✓ outermost section point 14.150 m from CL
Component chain with names	× 26 dimensions; names:	✓ 26 dimensions; names: B, CARRIAGEWAY, CORRIDOR WIDTH (LIMIT TO LIMIT),
Roadside / carriageway / corridor width dimensions	× rows 2 and 3 present	✓ rows 2 and 3 present
Architectural ticks on every dimension	× closed arrows	✓ Arrowhead type = architectural tick
Offset / level table and corridor limit markers	× 0 signed offset / level values	✓ 40 signed offset / level values

01 Install the add-in (1/3)

22/22 PASSED

Guide step	Check	Result	Status
1.1 package	**Add-in zip contents**	9/9 required files present	PASS
	Bundle carries the tested RoadPro.lsp	byte-identical to the tested file	PASS
	Plain package (APPLOAD) contents	6/6 files	PASS
1.1 PackageContents.xml	**PackageContents.xml is valid XML**	parsed without errors	PASS
	Runtime: AutoCAD 2013+ and all AutoCAD-based products	SeriesMin=R19.0, Platform=AutoCAD*	PASS
	Component points to RoadPro.lsp inside the bundle	ModuleName=./Contents/RoadPro.lsp	PASS
	Loads at start-up in every drawing	LoadOnAutoCADStartup=True, PerDocument=True	PASS
	Package identity	AppVersion=3.6.0, ProductCode={1BD9D2E3-6DF...	PASS
1.1 installer scripts	**Installer target = Autodesk ApplicationPlugins (per user, no admin)**	copies RoadPro.bundle to %APPDATA%\Autodesk\ApplicationPlugins	PASS

01 Install the add-in (2/3)

22/22 PASSED

Guide step	Check	Result	Status
1.1 installer scripts	Installer unblocks downloaded files	PowerShell Unblock-File on every copied file	PASS
	Installer stops if the bundle folder is missing	checks PackageContents.xml before copying	PASS
	Installer warns when AutoCAD is running	tasklist check for acad.exe	PASS
	Uninstaller removes the same folder	rmdir of the installed bundle	PASS
	Batch files use Windows line endings (CRLF)	CRLF	PASS
1.3 Start AutoCAD - load	RoadPro.lsp loads with no error	493 top-level forms evaluated, 0 errors	PASS
	Load message	prints "Road Pro v3.6 loaded … live update ON … RDHELP = all commands" + credit line	PASS
	Version constant	*rp:ver* = 3.6	PASS
	Functions defined	451 functions; 258 AutoCAD/ActiveX functions are mocked for this test	INFO

01 Install the add-in (3/3)

22/22 PASSED

Guide step	Check	Result	Status
1.4 Commands - menu and RDHELP	**Every listed command has its shortcut and full name**	22 commands, 22 complete	PASS
	RDHELP runs and lists all commands	22/22 commands printed, plus live-update and install state	PASS
	Helper commands exist	ROADPROLIVEUPDATE (used by live update) and ROADPRORESET are defined	PASS
1.5 Startup Suite method	**Install flag is kept per AutoCAD profile**	RoadPro_inst_Metric / RoadPro_inst_Imperial	PASS
	Startup Suite registry key	HKEY_CURRENT_USER\Software\Autodesk\AutoCAD\R24.3\ACAD-7101:409\Profiles\Imperial\Dialogs\Appload\Startup	PASS

02 Build a road (RDP) (1/2)

18/18 PASSED

Guide step	Check	Result	Status
2.1 Road Pro dialog	RDP dialog opens and OK works	opened 'roadpro' (54 tiles), 28 list items in 11 lists, all actions fired, OK -> OK; sub-dialogs opened and closed: roadcorr, roadpave	PASS
	RDP defaults	width 7.30 m, radius 10.0 m, chainage interval 20 m	PASS
2.2 road geometry	Change width 9.50, manual radius 15, millimetre units, select existing line	opened 'roadpro' (54 tiles), 28 list items in 11 lists, all actions fired, OK -> OK; sub-dialogs opened and closed: roadcorr, roadpave	PASS
	Change width 9.50, manual radius 15, millimetre units, select existing line - settings saved	saved: width=9.50, rmode=1, radius=15, units=1, mode=1	PASS
	ROADPRORESET restores the defaults	after reset: width 7.30, units 0; message: Road Pro settings restored to defaults (width 7.30 m, radius 10 m).	PASS
	Invalid road width is refused	OK refused, message shown: "Road width must be a number greater than zero."	PASS
	Zero road width is refused	OK refused, message shown: "Road width must be a number greater than zero."	PASS
2.3 edges, signs, markings	Cones, centre barricades, permanent signs, GIVE WAY at the tie-in	opened 'roadpro' (54 tiles), 28 list items in 11 lists, all actions fired, OK -> OK; sub-dialogs opened and closed: roadcorr, roadpave	PASS
	Cones, centre barricades, permanent signs, GIVE WAY at the tie-in - settings saved	saved: etype=1, ctype=1, sset=0, jctl=1, sspeed=0	PASS

02 Build a road (RDP) (2/2)

18/18 PASSED

Guide step	Check	Result	Status
2.4 surface, chainage, ends	Chainage every 50 m from 1+250, road closed at the end, no hatch	opened 'roadpro' (54 tiles), 28 list items in 11 lists, all actions fired, OK -> OK; sub-dialogs opened and closed: roadcorr, roadpave	PASS
	Chainage every 50 m from 1+250, road closed at the end, no hatch - settings saved	saved: chint=50, chst=1+250, endfn=1, hatch=0	PASS
	Chainage input parsing (rp:dist)	"0+100" -> 100.0; "1+250.5" -> 1250.5; "+100" -> 100.0; "250" -> 250.0; " 2+000 " -> 2000.0; "abc" -> nil; "1+x" -> nil	PASS
	Chainage labels (rp:chfmt) with DIMZIN=0	0.0 -> 0+000; 100.0 -> 0+100; 1250.5 -> 1+250.500; 12345.0 -> 12+345; 5.25 -> 0+005.250	PASS
	Chainage labels (rp:chfmt) with DIMZIN=8	0.0 -> 0+000; 100.0 -> 0+100; 1250.5 -> 1+250.5; 12345.0 -> 12+345; 5.25 -> 0+005.25	PASS
	Chainage labels (rp:chfmt) with DIMZIN=12	0.0 -> 0+000; 100.0 -> 0+100; 1250.5 -> 1+250.5; 12345.0 -> 12+345; 5.25 -> 0+005.25	PASS
2.5 centre line geometry	Arc centre from bulge (rp:arc-centre) vs reference	200 random arcs, 0 mismatches (tolerance 1e-7 m)	PASS
	Polyline sampling with arcs (rp:pl-sample)	61 points, max difference 2.7e-14 m	PASS
	Polygon area (rp:parea)	10 x 5 rectangle -> 50.000 m2	PASS

03 Corridor, pavement & quantities (1/3)

21/21 PASSED

Guide step	Check	Result	Status
3.1 RDC - corridor dialog	**Corridor dialog opens, Check layout runs, OK works**	opened 'roadcorr' (41 tiles), 14 list items in 5 lists, all actions fired, OK -> OK	PASS
	Dual carriageway, 2 + 2 lanes, 3 m median	opened 'roadcorr' (41 tiles), 14 list items in 5 lists, all actions fired, OK -> OK	PASS
3.2 RDPV - pavement dialog	**Pavement dialog - Flexible (asphalt)**	opened 'roadpave' (23 tiles), 3 list items in 1 lists, all actions fired, OK -> OK	PASS
	Pavement dialog - Flexible (asphalt) - settings saved	saved: ptype=0	PASS
	Pavement dialog - Concrete JPCP	opened 'roadpave' (23 tiles), 3 list items in 1 lists, all actions fired, OK -> OK	PASS
	Pavement dialog - Concrete JPCP - settings saved	saved: ptype=1	PASS
	Pavement dialog - Concrete JRCP with mesh	opened 'roadpave' (23 tiles), 3 list items in 1 lists, all actions fired, OK -> OK	PASS
	Pavement dialog - Concrete JRCP with mesh - settings saved	saved: ptype=2	PASS
3.3 Concrete quantities	**Concrete slab quantity**	plugin: 250 mm C40, area 1660.00 m2, volume 415.00 m3 | hand calc: 415.00 m3	PASS

03 Corridor, pavement & quantities (2/3)

21/21 PASSED

Guide step	Check	Result	Status
3.3 Concrete quantities	Stone base quantity	plugin: 200 mm CRUSHED STONE BASE, volume 332.00 m3 | hand calc: 332.00 m3	PASS
	Earthwork quantity	plugin: 300 mm EARTHWORK FILL 95% MDD, formation 1660.00 m2, volume 498.00 m3 | hand calc: 498.00 m3	PASS
	Dowel bars quantity	plugin: dia 32 x 450 mm @ 300 mm : 1188 nos, 3379.2 kg | hand calc: 1188 nos, 3379.2 kg	PASS
	Tie bars quantity	plugin: dia 16 x 800 mm @ 750 mm : 800 nos, 1011.4 kg | hand calc: 800 nos, 1011.4 kg	PASS
	TOTAL steel quantity	plugin: 4.391 t | hand calc: 4.391 t	PASS
	Steel unit weight $d^2/162$ kg/m	Ø32 = 6.32 kg/m (table 6.31), Ø16 = 1.58 kg/m (table 1.58)	PASS
	JRCP steel mesh incl. 10% laps	plugin: A393 (6.16 kg/m2) incl. 10% laps : 1826.0 m2, 11248.2 kg | hand calc: 1826.0 m2, 11248.2 kg	PASS
	Flexible pavement layer volumes	ASPHALT WEARING COURSE: 50 mm, area 1660.00 m2, volume 83.00 m3; AGGREGATE BASE COURSE: 200 mm, area 1660.00 m2, volume 332.00 m3; GRANULAR SUB-BASE: 150 mm, area 1660.00 m2, volume…	PASS
	Longitudinal joints - 2 lanes	offsets (0.0) (centre line)	PASS

03 Corridor, pavement & quantities (3/3)

21/21 PASSED

Guide step	Check	Result	Status
3.3 Concrete quantities	**Longitudinal joints - 4 lanes**	offsets (-3.65 0.0 3.65)	PASS
3.4 RDX - cross sections	**Cross-section dialog - typical section**	opened 'roadxsec' (20 tiles), 8 list items in 3 lists, all actions fired, OK -> OK	PASS
	Cross-section dialog - every chainage interval, 3% one-way	opened 'roadxsec' (20 tiles), 8 list items in 3 lists, all actions fired, OK -> OK	PASS

04 Widening & tapers

5/5 PASSED

Guide step	Check	Result	Status
4.1 RDW - lane widening	**Widening dialog - right side +3.65 m, CH 100-200**	opened 'roadwiden' (23 tiles), 7 list items in 3 lists, all actions fired, OK -> OK	PASS
	End chainage before start is refused	OK refused, message shown: "End chainage must be greater than the start chainage."	PASS
4.2 RDT - taper	**Taper dialog - both sides +1.00 m**	opened 'roadtaper' (18 tiles), 7 list items in 3 lists, all actions fired, OK -> OK	PASS
	Taper dialog - narrower road (-0.50 m)	opened 'roadtaper' (18 tiles), 7 list items in 3 lists, all actions fired, OK -> OK	PASS
	Taper end before start is refused	OK refused, message shown: "Taper end chainage must be greater than the start chainage."	PASS

05 Junctions & Saudi standard (1/2)

16/16 PASSED

Guide step	Check	Result	Status
5.1 junction dialog	Junction dialog - manual priority junction	opened 'roadjunc' (28 tiles), 33 list items in 8 lists, all actions fired, OK -> OK; sub-dialogs opened and closed: roadrbt	PASS
5.2 Saudi standard values	Class 1 (P) at 60 km/h	R 9.0 m, lane 3.0 m, approach taper 30 m, departure 25 m, storage 65 m, island 1.8 x 15 m, tg 7.5 s	PASS
	Class 1 values fill the dialog and are saved	saved corner radius 9.0, aux lane 3.00, sight triangles 1	PASS
	Class 2 (SU) at 60 km/h	R 12.0 m, lane 3.5 m, approach taper 35 m, departure 30 m, storage 60 m, island 1.8 x 15 m, tg 9.5 s	PASS
	Class 2 values fill the dialog and are saved	saved corner radius 12.0, aux lane 3.50, sight triangles 1	PASS
	Class 3 (WB-15) at 60 km/h	R 15.0 m, lane 3.65 m, approach taper 40 m, departure 30 m, storage 55 m, island 2.4 x 15 m, tg 11.5 s	PASS
	Class 3 values fill the dialog and are saved	saved corner radius 15.0, aux lane 3.65, sight triangles 1	PASS
	Class 4 (WB-19) at 60 km/h	R 18.0 m, lane 3.65 m, approach taper 40 m, departure 30 m, storage 55 m, island 2.4 x 15 m, tg 11.5 s	PASS
	Class 4 values fill the dialog and are saved	saved corner radius 18.0, aux lane 3.65, sight triangles 1	PASS

05 Junctions & Saudi standard (2/2)

16/16 PASSED

Guide step	Check	Result	Status
5.2 Saudi standard values	Intersection sight distance ISD = 0.278 V tg	60 km/h, tg 7.5 s -> 125 m (AASHTO 125 m); 60 km/h, tg 9.5 s -> 158 m (AASHTO 158 m); 60 km/h, tg 11.5 s -> 192 m (AASHTO 192 m); 80 km/h, tg 7.5 s -> 167 m (AASHTO 167 m)	PASS
5.3 roundabout type	Junction type = Roundabout, More roundabout settings	opened 'roadjunc' (28 tiles), 33 list items in 8 lists, all actions fired, OK -> OK; sub-dialogs opened and closed: roadrbt	PASS
	Inscribed radius too small is refused	OK refused, message shown: "The inscribed radius must be more than half the branch width + 1 m."	PASS
5.4 Junction corners - corridor wrap	Corner wrap R=10 m, branch at 90°	sidewalk / walkway / drain / utility: overlap 0.000 m², 2 corner pieces each	PASS
	Corner wrap R=15 m, branch at 90°	sidewalk / walkway / drain / utility: overlap 0.000 m², 2 corner pieces each	PASS
	Corner wrap R=10 m, branch at 70°	sidewalk / walkway / drain / utility: overlap 0.000 m², 2 corner pieces each	PASS
	Half-plane clipping (rp:clip-half)	10 x 10 square clipped at x = 5 -> 4 vertices, x from 5.0 to 10.0	PASS

06 Roundabouts (1/3)

22/22 PASSED

Guide step	Check	Result	Status
6.1 Roundabout standards	13 standards in the list (Manual + 8 FHWA 2000 + 4 Guide 2010)	13 rows	PASS
	Default ICD inside the guide range for every standard	all 12 standards: ICD min <= default <= max	PASS
	Urban Double Lane Spiral (default) values	R 25.00, circ. width 9.50, apron 2.00, entry/exit 30.00/40.00, lanes index 1, spiral 1	PASS
	FHWA 2000: Mini Roundabout	pick in RDRB -> saved R 11.00 m (ICD 22), circ. width 5.00 m, entry 10.00 m, exit 15.00 m	PASS
	FHWA 2000: Rural Double Lane Roundabout	pick in RDRB -> saved R 29.00 m (ICD 58), circ. width 10.00 m, entry 35.00 m, exit 50.00 m	PASS
	FHWA 2000: Rural Double Lane Spiral Marking Roundabout	pick in RDRB -> saved R 29.00 m (ICD 58), circ. width 10.00 m, entry 35.00 m, exit 50.00 m	PASS
	FHWA 2000: Rural Single Lane Roundabout	pick in RDRB -> saved R 19.00 m (ICD 38), circ. width 5.50 m, entry 25.00 m, exit 40.00 m	PASS
	FHWA 2000: Urban Compact Roundabout	pick in RDRB -> saved R 14.00 m (ICD 28), circ. width 5.00 m, entry 12.00 m, exit 15.00 m	PASS
	FHWA 2000: Urban Double Lane Roundabout	pick in RDRB -> saved R 25.00 m (ICD 50), circ. width 9.50 m, entry 30.00 m, exit 40.00 m	PASS

06 Roundabouts (2/3)

22/22 PASSED

Guide step	Check	Result	Status
6.1 Roundabout standards	FHWA 2000: Urban Double Lane Spiral Marking Roundabout	pick in RDRB -> saved R 25.00 m (ICD 50), circ. width 9.50 m, entry 30.00 m, exit 40.00 m	PASS
	FHWA 2000: Urban Single Lane Roundabout	pick in RDRB -> saved R 17.50 m (ICD 35), circ. width 5.50 m, entry 20.00 m, exit 30.00 m	PASS
	Guide 2010 (NCHRP 672): Mini-Roundabout	pick in RDRB -> saved R 11.00 m (ICD 22), circ. width 5.00 m, entry 10.00 m, exit 15.00 m	PASS
	Guide 2010 (NCHRP 672): Single-Lane Roundabout	pick in RDRB -> saved R 20.00 m (ICD 40), circ. width 5.50 m, entry 20.00 m, exit 30.00 m	PASS
	Guide 2010 (NCHRP 672): Multilane Roundabout	pick in RDRB -> saved R 27.50 m (ICD 55), circ. width 9.50 m, entry 30.00 m, exit 45.00 m	PASS
	Guide 2010 (NCHRP 672): Multilane Spiral Marking	pick in RDRB -> saved R 27.50 m (ICD 55), circ. width 9.50 m, entry 30.00 m, exit 45.00 m	PASS
6.2 RDRB - roundabout dialog	Roundabout dialog - both side roads, draw new	opened 'roadrbt' (26 tiles), 24 list items in 5 lists, all actions fired, OK -> OK	PASS
	Roundabout radius smaller than the circulatory width is refused	OK refused, message shown: "The circulatory width must be smaller than the inscribed radius."	PASS
6.3 Roundabout geometry	Entry fillets tangent to the circle - LISP matches reference	120 leg/corner cases over 12 standards x T, cross and Y layouts; max difference 0.0e+00 m	PASS

06 Roundabouts (3/3)

22/22 PASSED

Guide step	Check	Result	Status
6.3 Roundabout geometry	**Splitter islands leave at least 3 m entry lane**	132 sections along the islands of 12 standards; LISP = reference; kerb-to-island >= 3.0 m	PASS
6.4 Regression - bugs found by this test	**Entry fillet touches the inscribed circle (R 25, entry r 30)**	tangent point 25.000 m from the centre (was 30.000 m before the fix: R and r are the same AutoLISP variable)	PASS
	Side road is fitted to the circle (rp:rb-fit)	runs (before the fix: "bad argument type" - the centre O was overwritten by the local o)	PASS
	No function mixes names that differ only by upper / lower case	none (the unused sB / sb pair in rp:junction-run was removed in v3.6)	PASS

07 Edit & live update

5/5 PASSED

Guide step	Check	Result	Status
7.1 RDLIVE - live update switch	**RDLIVE Off**	setting live = 0; message: RoadPro LIVE update is OFF : run RDB after editing a centre line....	PASS
	RDLIVE On	setting live = 1; message: RoadPro LIVE update is ON : grip-edit / MOVE / ROTATE / STRETCH / PEDIT a road centre line...	PASS
	Live-update wiring	present: object reactor on centre lines, command reactor (commandEnded), cancel / fail handled, rebuild sent as a command, re-entry guard while rebuilding	PASS
	Replay of widenings, tapers, junctions, roundabouts	rp:replay-w, rp:replay-t, rp:replay-j, rp:replay-r, rp:rebuild, rp:move-branches, rp:live-process defined	PASS
7.2 RDB / RDER / RDU	**Rebuild and edit commands defined**	RDB, RDER, RDU and their full names are defined	PASS

08 Lines, labels & exchange

3/3 PASSED

Guide step	Check	Result	Status
8.1 RDL - single line	**Single-line dialog - barricades, offset 0.50**	opened 'roadline' (12 tiles), 7 list items in 2 lists, all actions fired, OK -> OK	PASS
	Single-line dialog - cones, from 10 m to 80 m	opened 'roadline' (12 tiles), 7 list items in 2 lists, all actions fired, OK -> OK	PASS
8.2 RDM / RDRAD / RDSEC / LandXML	**Commands defined**	RDM, RDRAD, RDSEC, RDLX, RDLXI	PASS

09 Code checks, shortcuts & guide

9/9 PASSED

Guide step	Check	Result	Status
9.1 Code checks	Brackets balanced in all 493 forms	parser read every form	PASS
	No call to an undefined function	none	PASS
	No wrong number of arguments	every call matches its defun	PASS
	DCL braces balanced in all dialogs	9 dialogs: *rp:dcl* 67/67, *rp:xdcl* 27/27, *rp:wdcl* 25/25, *rp:tdcl* 22/22, *rp:jdcl* 38/38, *rp:cdcl* 57/57, *rp:ldcl* 15/15, *rp:rbdcl* 33/33, *rp:pdcl* 30/30	PASS
	Local variables declared	5 notes, all false alarms: 4 are ActiveX constants (vlax-vbDouble ...), 1 is a lambda-local the checker does not see	PASS
9.2 Shortcuts sheet and guide	Shortcuts sheet lists every command	22/22 shortcuts found	PASS
	Shortcuts sheet dated 11-Nov-2026	dates found: ['11-Nov-2026']	PASS
	Every command named in the user guide exists	45 command names in the guide, all defined	PASS
	Guide covers every command	22/22 commands appear in the guide	PASS

10 v3.6 error report — drawing tests (1/4)

34/34 PASSED

Guide step	Check	Result	Status
10.1 Junction 90 deg, aux lane + island	**Road surface hatches do not overlap (one clean mouth)**	4 surface hatches, overlap 0.00 m2	PASS
	No barricade inside the carriageways	416 barricade units, 0 inside a travelled way	PASS
	Barricade units do not overlap	0 overlapping pairs	PASS
	Sidewalk strips meet the corner pieces	sidewalk: 48 hatches in 3 connected group(s), overlap 0.00 m2	PASS
	Walkway strips meet the corner pieces	walkway: 48 hatches in 3 connected group(s), overlap 0.00 m2	PASS
	RDB rebuild keeps the junction unchanged	1653 -> 1653 objects	PASS
	Move the main centre line : junction follows	surface overlap 0.00 m2, branch head start y 7.30 -> 12.30 m (+5 expected)	PASS
10.1 Junction 60 deg skew, R 30	**Road surface hatches do not overlap (one clean mouth)**	3 surface hatches, overlap 0.00 m2	PASS
	No barricade inside the carriageways	401 barricade units, 0 inside a travelled way	PASS

10 v3.6 error report — drawing tests (2/4)

34/34 PASSED

Guide step	Check	Result	Status
10.1 Junction 60 deg skew, R 30	Barricade units do not overlap	0 overlapping pairs	PASS
	Sidewalk strips meet the corner pieces	sidewalk: 45 hatches in 3 connected group(s), overlap 0.00 m2	PASS
	Walkway strips meet the corner pieces	walkway: 45 hatches in 3 connected group(s), overlap 0.00 m2	PASS
10.2 Roundabout 3-way (T)	Main road surface is cut at the ring (no double hatch)	4 surface hatches, overlap 0.00 m2	PASS
	No barricade runs into the roundabout	398 barricade units, 0 inside the ring	PASS
	Barricade units do not overlap	0 overlapping pairs	PASS
	Sidewalk hatches do not overlap	55 hatches, overlap 0.00 m2	PASS
	Full marking drawn	303 marking objects (edge lines, ring line, arrows, give way)	PASS
10.2 Roundabout 4-way (cross)	Main road surface is cut at the ring (no double hatch)	5 surface hatches, overlap 0.00 m2	PASS

10 v3.6 error report — drawing tests (3/4)

34/34 PASSED

Guide step	Check	Result	Status
10.2 Roundabout 4-way (cross)	No barricade runs into the roundabout	496 barricade units, 0 inside the ring	PASS
	Barricade units do not overlap	0 overlapping pairs	PASS
	Sidewalk hatches do not overlap	72 hatches, overlap 0.00 m2	PASS
	Full marking drawn	229 marking objects (edge lines, ring line, arrows, give way)	PASS
10.3 Roundabout - automatic 4-way legs	Two side roads made at 90 degrees, 70 m	2 side roads ending at (150, +/-70)	PASS
	No barricade inside the ring or overlapping	396 units, 0 overlapping	PASS
10.4 Curve edit (grip) + live update	Grip vertex: curve stays tangent	largest kink at a curve end 0.00 deg	PASS
	Grip vertex: barricades follow without crossing	314 units, 0 overlapping pairs	PASS
	Grip bulge: curve stays tangent	largest kink at a curve end 0.00 deg	PASS

10 v3.6 error report — drawing tests (4/4)

34/34 PASSED

Guide step	Check	Result	Status
10.4 Curve edit (grip) + live update	**Grip bulge: barricades follow without crossing**	318 units, 0 overlapping pairs	PASS
	RDER radius 60 : barricades follow	radii now [30.0, 60.0], 0 overlapping barricade pairs	PASS
10.5 Cross section - corridor limit + dimensions	**Section geometry stops at the corridor limit (14.15 m)**	outermost section point 14.150 m from CL	PASS
	Component chain with names	26 dimensions; names: B, CARRIAGEWAY, CORRIDOR WIDTH (LIMIT TO LIMIT), DR, LANE, LEFT ROADSIDE, RIGHT ROADSIDE, SH, SIDEWALK, UTILITY, VG, WALKWAY	PASS
	Roadside / carriageway / corridor width dimensions	rows 2 and 3 present	PASS
	Architectural ticks on every dimension	Arrowhead type = architectural tick	PASS
	Offset / level table and corridor limit markers	40 signed offset / level values	PASS

Dialog coverage

ALL 9 DIALOGS

Command	Dialog	Tiles checked	Lists / items	Opens sub-dialog	All actions fired	OK closes	Bad input refused
RDP	`roadpro`	54	11 / 28	roadcorr, roadpave	✓	✓	✓ width
RDC	`roadcorr`	41	5 / 14	—	✓	✓	—
RDPV	`roadpave`	23	1 / 3	—	✓	✓	—
RDX	`roadxsec`	20	3 / 8	—	✓	✓	—
RDW	`roadwiden`	23	3 / 7	—	✓	✓	✓ chainage
RDT	`roadtaper`	18	3 / 7	—	✓	✓	✓ chainage
RDJ	`roadjunc`	28	8 / 33	roadrbt	✓	✓	✓ radius
RDRB	`roadrbt`	26	5 / 24	—	✓	✓	✓ circ. width
RDL	`roadline`	12	2 / 7	—	✓	✓	—

RESULT Every set_tile, get_tile, mode_tile and action_tile call was matched against the dialog file: 0 unknown keys, 0 empty lists, 0 errors.

AutoCAD field-test checklist (1/2)

TO DO IN AUTOCAD

#	Guide step	Do this	Expected	Pass	Fail	Notes
1	1.1	Run Install_RoadPro.bat (v3.6), start AutoCAD	"Road Pro v3.6 loaded" on the command line	☐	☐	
2	10.1	RDJ 90° with aux lane + island (picture 1)	Branch starts at the kerb returns; walkway / sidewalk strips meet the corners	☐	☐	
3	10.1	RDJ 60° skew R 30 (picture 2)	One mouth hatch joined to the main hatch — no overlap, no wedges	☐	☐	
4	10.1	RDB on an old v3.5 road with a junction	Junction redrawn with the clean tie-in	☐	☐	
5	10.2	RDRB 3-way (T) on a road (picture 3)	Main road hatch / barricades / edge lines stop at the ring	☐	☐	
6	10.2	RDRB 4-way, full marking (picture 4)	Edge lines, ring line, arrows, give way on every leg	☐	☐	
7	10.3	RDRB 4-way, side roads Automatic, 70 m	Two straight side roads at 90°, full roads	☐	☐	
8	10.4	Grip-drag a bend midpoint; then RDER R 60 (picture 5)	Bend stays tangent; barricades follow the curve	☐	☐	
9	10.1	MOVE the main centre line 5 m (live update ON)	Junction / roundabout follow; U undoes	☐	☐	

AutoCAD field-test checklist (2/2)

#	Guide step	Do this	Expected	Pass	Fail	Notes
10	10.5	RDX typical section	Stops at corridor limit; 3 dimension rows; level table	☐	☐	
11	10.5	RDX every 20 m	Sections in a grid, no overlap	☐	☐	
12	6.1	RDRB with Mini, Urban single, Rural double	Values of each standard; drawing completes	☐	☐	
13	3.3	RDPV concrete JPCP, then RDX	Slab, base, earthwork and steel in the section	☐	☐	
14	2.5	RDP: pick points, 2 bends	Edges, barricades, markings, chainage, signs, curve labels	☐	☐	
15	4.1	RDW right +3.65 m, CH 100–200	Widening with tapers, barricades moved	☐	☐	
16	7.2	RDB / RDER on a road with widening + junction	Everything replayed	☐	☐	
17	8.2	RDLX then RDLXI in Civil 3D	LandXML round trip	☐	☐	
18	1.5	Run Uninstall_RoadPro.bat, restart	RoadPro no longer loads	☐	☐	

Tested. Fixed. Ready for AutoCAD.


RoadPro v3.6 — test report 11-Nov-2026

Updated files

RoadPro.lsp v3.6 — all 9 items of the error report

RoadPro_v3.6_AddIn.zip and RoadPro_v3.6.zip — plugin, guide, shortcuts, report

Next: run the field-test checklist on a copy of a drawing

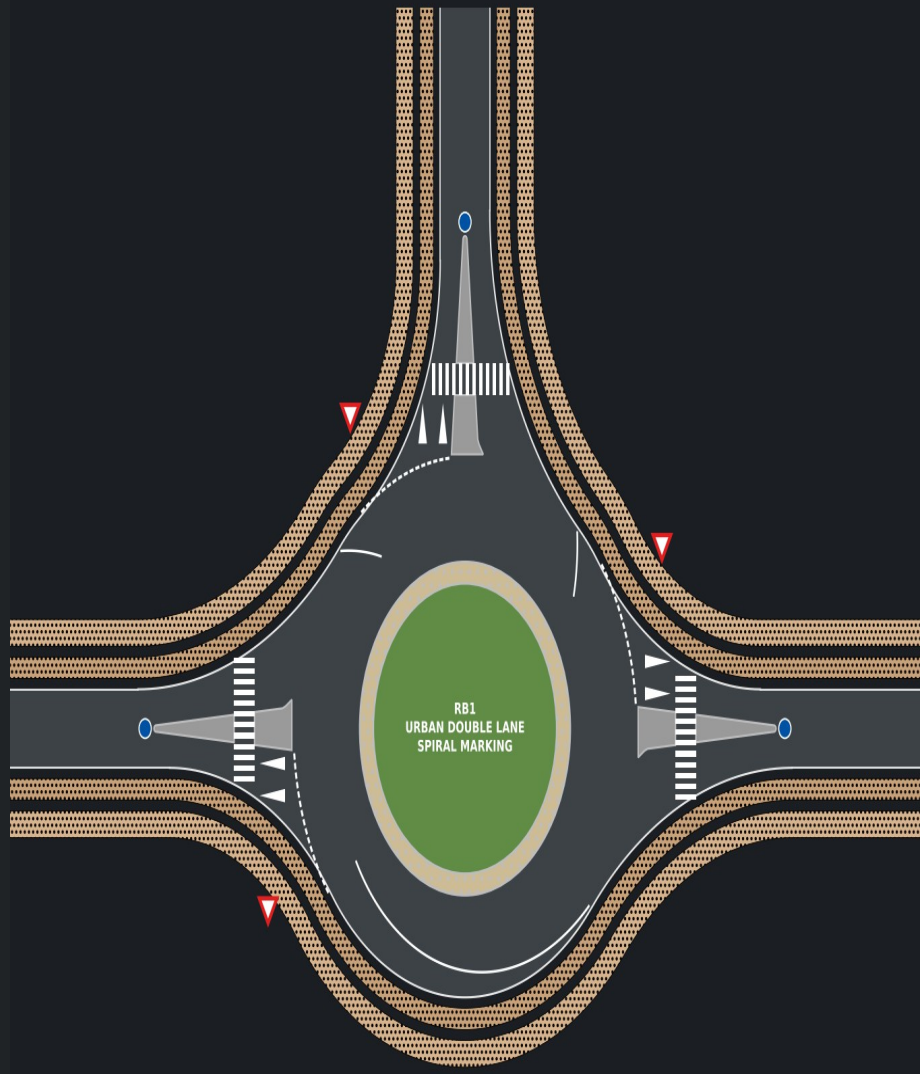

Developed by https://www.exceltokml.com/
